

Project Planning Phase

Project Planning Template (Product Backlog, Sprint Planning, Stories, Story Points)

Date	1 October 2026
Team ID	SWTID-2026-8542
Project Name	ComicCraft – AI Comic Story Creator using Gemini Models
Maximum Marks	5 Marks

Product Backlog, Sprint Schedule, and Estimation (4 Marks)

The following backlog converts the ComicCraft project idea into small, testable user stories. Story points represent relative effort and complexity.

Sprint	Functional Requirement	User Story Number	User Story / Task	Story Points	Priority	Team Members
Sprint-1	Registration / Login	USN-1	As a user, I can create an account and log in securely so that I can access my ComicCraft projects.	3	High	Project Team
Sprint-1	Story Creation	USN-2	As a creator, I can enter a theme, characters, setting and plot idea so that Gemini can generate a comic story.	5	High	Project Team
Sprint-1	Story Creation	USN-3	As a creator, I can select genre, tone and story length so that the generated story matches my requirements.	3	Medium	Project Team
Sprint-2	AI Story Generation	USN-4	As a creator, I can generate a structured comic script using Gemini models with scenes, dialogue and narration.	5	High	Project Team
Sprint-2	Character Design	USN-5	As a creator, I can define character descriptions and roles so that characters remain consistent across the comic.	3	High	Project Team
Sprint-2	Panel Generation	USN-6	As a creator, I can generate comic-panel prompts/images for each scene so that the story becomes visually readable.	5	High	Project Team
Sprint-3	Editor / Preview	USN-7	As a creator, I can edit dialogue, narration and panel order before finalizing the comic.	3	Medium	Project Team
Sprint-3	Regeneration	USN-8	As a creator, I can regenerate a selected scene or panel when the output does not match my requirement.	3	Medium	Project Team
Sprint-3	Save Projects	USN-9	As a creator, I can save and reopen comic projects so that my work is not lost.	3	High	Project Team
Sprint-4	Export	USN-10	As a creator, I can export the completed comic in a shareable format such as PDF/images.	3	High	Project Team
Sprint-4	Testing & Deployment	USN-11	As a project team, we can test generation, editing, saving and export workflows and deploy the working application.	5	High	Project Team

Total planned story points: 41. The backlog can be adjusted after Sprint-1 based on actual team capacity and feedback.

Project Tracker, Velocity & Burndown Chart

Sprint tracker for ComicCraft – AI Comic Story Creator using Gemini Models

Sprint	Total Story Points	Sprint Duration	Sprint Start Date	Sprint End Date	Story Points Completed	Sprint Release Date
Sprint-1	11	10 Days	05 Oct 2026	16 Oct 2026	11	16 Oct 2026
Sprint-2	13	10 Days	19 Oct 2026	30 Oct 2026	13	30 Oct 2026
Sprint-3	9	10 Days	02 Nov 2026	13 Nov 2026	9	13 Nov 2026
Sprint-4	8	10 Days	16 Nov 2026	27 Nov 2026	8	27 Nov 2026

Velocity:


Assume the team completes an average of 20 story points in a 10-day sprint. Average velocity per working day can be calculated as:

$$\text{Average Velocity per Day} = \text{Story Points Completed} \div \text{Sprint Duration} = 20 \div 10 = 2 \text{ story points/day}$$

This value is used only as a planning estimate. Actual velocity should be updated from completed stories at the end of each sprint.

Burndown Chart:

A burndown chart shows the amount of work remaining over time. For ComicCraft, the horizontal axis represents sprint days and the vertical axis represents remaining story points. The ideal line shows planned progress, while the actual line shows the team's real progress.

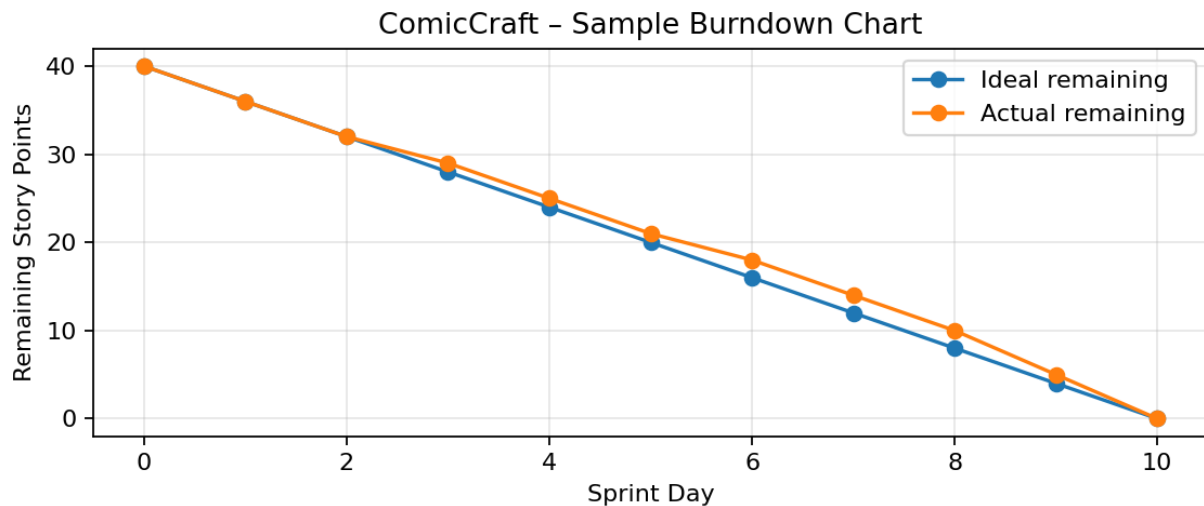

ComicCraft – Project Planning Summary

Scope, Sprint Goals, Deliverables and References

Project Objective

ComicCraft is an AI-assisted comic story creation application that helps users turn an idea into a structured comic. The planned workflow is: user input → story generation → character/scene planning → comic panel generation → editing and preview → export/share. Gemini models are used as the generative AI component for the planned story and creative workflows.

Sprint-wise Goals

Sprint	Goal	Expected Deliverables
Sprint-1	Foundation & User Input	Login/registration, project creation form, genre/tone selection, initial database/project structure.
Sprint-2	AI Generation	Gemini-based story/script generation, character descriptions, scene breakdown and panel-generation workflow.
Sprint-3	Editing & Persistence	Comic editor/preview, regenerate selected content, save/reopen projects, validation and error handling.
Sprint-4	Export, Testing & Deployment	PDF/image export, end-to-end testing, bug fixing, deployment-ready build and final demonstration.

Definition of Done

Area	Completion Criteria
Story Generation	Valid user input produces a structured story with scenes, narration and dialogue.
Comic Panels	Each selected scene has an associated panel prompt/output and can be previewed.
Editing	User can modify text/panel order and regenerate selected content.
Storage	Project can be saved and reopened without losing completed work.
Export	Completed comic can be exported into the planned shareable format.
Testing	Core workflows are tested and major errors are handled before deployment.

Key Risks & Mitigation

Risk	Mitigation
AI output may not match the user's idea	Use structured prompts, editable fields and scene/panel regeneration.
Character consistency may vary	Maintain reusable character descriptions and pass them into scene prompts.
Generation latency or failures	Show progress/error states, allow retry, and save completed sections incrementally.
Unexpected or unsuitable generated content	Apply input validation, safety controls and human review before final export.

References / Learning Resources

- Google Gemini documentation and developer resources – for Gemini model capabilities and API concepts.
- Google Cloud Vertex AI documentation – for generative AI application development concepts.
- Scrum Guide – for product backlog, sprint planning, sprint review and iterative development concepts.

Note: Dates, story points and team-member entries are sample planning values created to fit the supplied template. They can be replaced with your actual college project team details before submission.
